LOOK AHEAD SCHEDULE

PROJECT: DC PLUG FEEDER 15009 Civil Construction

CAPITOL PAVING OF D.C., INC

Week Start: Wed, 7/10/2024
Today Date: Wed, 7/10/2024
Display Week: 1
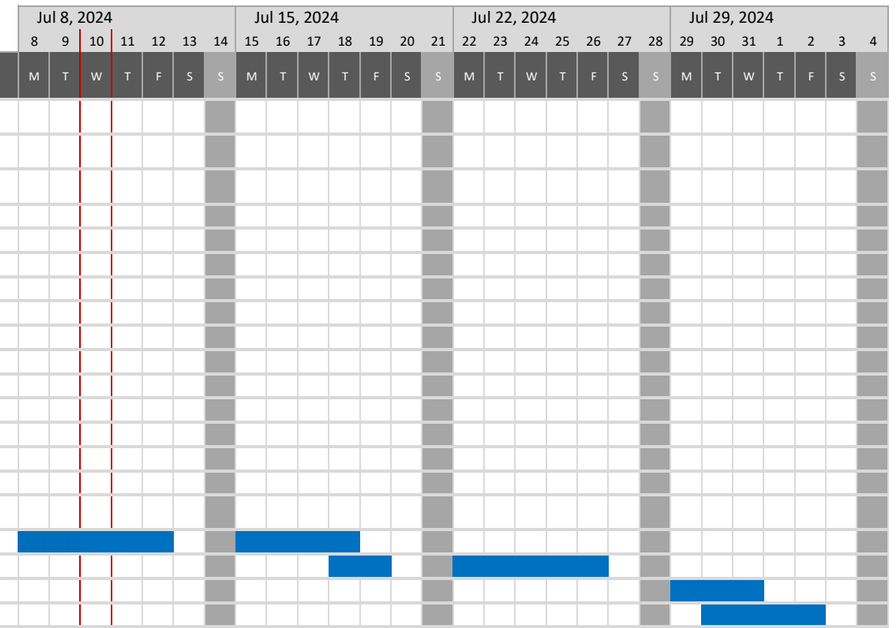
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
	DCKA-2022-C-0036.3 Submittals and Shop Drawings				**2/15/2023**		**511**
	DCKA-2022-C-0036.6 Pre-Construction				**2/28/2023**		**498**
PHASE	**DCKA-2022-C-0036-1.7.1.1.1 PH1 STRUCTURE - COMPLETED**				**5/30/2023**	**8/9/23**	**71**
PHASE	**DCKA-2022-C-0036-1.7.1.1 Phase 1 - Utility - COMPLETED**				**5/30/2023**	**9/29/23**	**122**
PHASE	**DCKA-2022-C-0036-1.7.2.1 Phase 1 - Pavement - COMPLETED**				**9/18/2023**	**11/11/23**	**54**
PHASE	**DCKA-2022-C-0036.7.1.2.1 PH2 STRUCTURE MOD - COMPLETED**				**3/20/2023**	**5/12/23**	**53**
PHASE	**DCKA-2022-C-0036.7.1.2 Phase 2 - Utility - COMPLETED**				**3/20/2023**	**8/10/23**	**143**
PHASE	**DCKA-2022-C-0036-1.7.2.2 Phase 2 - Pavement - COMPLETED**				**6/7/2023**	**9/13/23**	**98**
PHASE	**DCKA-2022-C-0036-1.7.1.3.1 PH3 STRUCTURE - COMPLETED**				**6/13/2023**	**10/31/23**	**140**
PHASE	**DCKA-2022-C-0036-1.7.2.3 Phase 3 Utility - COMPLETED**				**6/13/2023**		**-45090**
PHASE	**DCKA-2022-C-0036-1.7.2.4 Phase 3 Pavement - COMPLETED**				**12/15/2023**		**208**
PHASE	**DCKA-2022-C-0036-1.7.1.4.1 PHASE 4 STRUCTURE - COMPLETED**				**6/13/2023**	**10/31/23**	**140**
PHASE	**DCKA-2022-C-0036-1.7.1.4 Phase 4 - Utility - COMPLETED**				**8/7/2023**	**12/5/23**	**120**
PHASE	**DCKA-2022-C-0036-1.7.2.4 Phase 4 Pavement - COMPLETED**				**10/10/2023**		**274**
	DCKA-2022-C-0036-1.8 Substantial Completion						
	CO-1060 Install Structures and Conduit	CPDC	3rd St and Blair Rd, 7th St and Whittier St	20%	7/8/24	7/18/24	10.00
	CO-1070 Roadway Restoration	CPDC	3rd St and Blair Rd, 7th St and Whittier St	0%	7/18/24	7/26/24	8.00
	FNL1000-CO PEPCO Structures Inspection	CPDC	3rd St and Blair Rd, 7th St and Whittier St	0%	7/29/24	7/31/24	2.00
	Punch List Work - CO	CPDC	3rd St and Blair Rd, 7th St and Whittier St	0%	7/30/24	8/2/24	3.00
