LOOK AHEAD SCHEDULE

PROJECT: DC PLUG FEEDER 15009 Civil Construction

CAPITOL PAVING OF D.C., INC

Week Start: Mon, 4/8/2024
Today Date: Fri, 4/12/2024
Display Week: 1
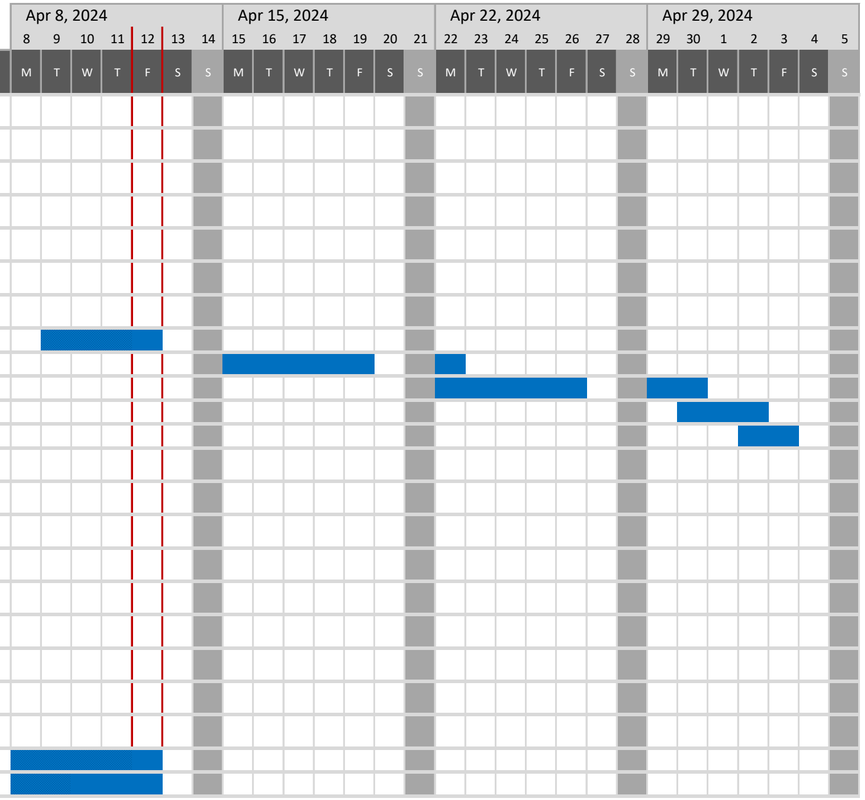
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
	DCKA-2022-C-0036.3 Submittals and Shop Drawings				**2/15/2023**		**422**
	DCKA-2022-C-0036.6 Pre-Construction				**2/28/2023**		**409**
PHASE 1	**DCKA-2022-C-0036-1.7.1.1.1 PH1 STRUCTURE - COMPLETED**				**5/30/2023**	**8/9/23**	**71**
PHASE 1	**DCKA-2022-C-0036-1.7.1.1 Phase 1 - Utility - COMPLETED**				**5/30/2023**	**9/29/23**	**122**
PHASE 1	**DCKA-2022-C-0036-1.7.2.1 Phase 1 - Pavement - COMPLETED**				**9/18/2023**	**11/11/23**	**54**
PHASE 2	**DCKA-2022-C-0036.7.1.2.1 PH2 STRUCTURE MOD - COMPLETED**				**3/20/2023**	**5/12/23**	**53**
PHASE 2	CO-1020 PH1 - Install Cast-In-Place MH 4.5x6 @2nd St (SB3)	ANCHOR		90%	4/9/24	4/12/24	3.00
PHASE 2	CO-1050 PH2 - Install Cast-In-Place 4.5x6 @ Van Buren (New)	ANCHOR		0%	4/13/24	4/22/24	9.00
PHASE 2	CO-1030 PH1 - Install Cast-In-Place MH 4.5x6 @5th St (SB4)	ANCHOR		0%	4/22/24	4/30/24	8.00
PHASE 2	CO-1040 PH1 - Install New SB @411 Rittenhouse St	ANCHOR		0%	4/30/24	5/2/24	2.00
PHASE 2	CO-1040 Restoration @ Newly Installed Structures	ANCHOR		0%	5/2/24	5/5/24	3.00
PHASE 2	**DCKA-2022-C-0036.7.1.2 Phase 2 - Utility - COMPLETED**				**3/20/2023**	**8/10/23**	**143**
PHASE 2	**DCKA-2022-C-0036-1.7.2.2 Phase 2 - Pavement - COMPLETED**				**6/7/2023**	**9/13/23**	**98**
PHASE 3	**DCKA-2022-C-0036-1.7.1.3.1 PH3 STRUCTURE - COMPLETED**				**6/13/2023**	**10/31/23**	**140**
PHASE 3	**DCKA-2022-C-0036-1.7.2.3 Phase 3 Utility - COMPLETED**				**6/13/2023**		**-45090**
PHASE 3	**DCKA-2022-C-0036-1.7.2.4 Phase 3 Pavement - COMPLETED**				**12/15/2023**		**119**
PHASE 4	**DCKA-2022-C-0036-1.7.1.4.1 PHASE 4 STRUCTURE - COMPLETED**				**6/13/2023**	**10/31/23**	**140**
PHASE 4	**DCKA-2022-C-0036-1.7.1.4 Phase 4 - Utility - COMPLETED**				**8/7/2023**	**12/5/23**	**120**
PHASE 4	**DCKA-2022-C-0036-1.7.2.4 Phase 4 Pavement - COMPLETED**				**10/10/2023**		**185**
	DCKA-2022-C-0036-1.8 Substantial Completion						
PHASE 5	FNL1000 PEPCO Structures Inspection		Various Locations	98%	3/25/24	4/12/24	18.00
PHASE 5	Punch List Work		Various Locations	80%	3/25/24	4/13/24	19.00
