Owner: **Government of the District of Columbia**
Department of Transportation

Project Name: **Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding (DC PLUG) Feeder 14758**
Contract No.: **DCKA-2022-C-0069**

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 9-Oct-23 **to:** 29-Oct-23 **Data Date:** 9-Oct-23

ID	Description	Location	Planned Start	Planned Finish	Actual % as of DD
Submittals and Shop Drawings			28-Sep-23		
General Requirements			28-Sep-23		
SUB1020	Submit Subcontractor Approval Request		9-Oct-23		50%
SUB1030	Engineer's Review & Approval - Subcontractors		9-Oct-23	14-Oct-23	0%
FAB1000	Order, Procure, and Pick- Up PEPCO Supplied Conduits, and Fittings (Joliet St & First St)		2-Oct-23	16-Feb-24	10%
FAB1010	Order, Procure, and Pick- Up PEPCO Supplied Conduits, and Fitting (Chesapeake St)		2-Oct-23	14-Nov-23	10%
FAB1020	Order, Procure, and Pick- Up PEPCO Supplied Conduits, and Fitting (MLK Ave & Ivanhoe Circle)		2-Oct-23	3-Jan-24	10%
Pre-Construction			28-Sep-23		
PRE1000	Construction Staging Area	4100 Block 2nd St. SW	10-Oct-23	15-Oct-23	
PRE1050	Project Mobilization		17-Oct-23	17-Oct-23	
Construction Work			28-Sep-23		
Joliet Street & First Street SW			28-Sep-23		
Utility			28-Sep-23		
A1020	Install MH#21 & MH#22	100 Block Joliet St. SW	17-Oct-23	17-Oct-23	
A1590	Install Conduit MH#20 to MH#21	100 Block Joliet St. SW	23-Oct-23	25-Oct-23	
A1600	Install MH#23 & MH#24	100 Block Joliet St. SW	17-Oct-23	18-Oct-23	
A1610	Install TAP#21	100 Block Joliet St. SW	19-Oct-23	19-Oct-23	
A1620	Install Conduit MH#22 to MH#23	100 Block Joliet St. SW	26-Oct-23	27-Oct-23	
A1650	Install Conduit MH#23 to MH#31	100 Block Joliet St. SW	28-Oct-23	30-Oct-23	
A1670	Install MH#25	100 Block Joliet St. SW	18-Oct-23	18-Oct-23	
A1670	Install MH#40	100 Block Joliet St. SW	18-Oct-23	18-Oct-23	
A1670	Install TE#11 & TE#14	100 Block Joliet St. SW	19-Oct-23	19-Oct-23	
A1680	Install MH#26	100 Block Joliet St. SW	20-Oct-23	20-Oct-23	
A1680	Install MH#27, TAP#17, TE#16	100 Block Joliet St. SW	20-Oct-23	21-Oct-23	
Pavement Restoration			15-Jul-23		
Chesapeake St. SW			23-Oct-23		
Utility			23-Oct-23		
A1040	Install MH#7 & TMH#1	Unit Block Chesapeake St. SW	23-Oct-23	26-Oct-23	
A1080	Install TE#3, TAP#4, & TE#2	100 Block Chesapeake St. SW	27-Oct-23	27-Oct-23	
A1120	Install TE#1 & TAP#3	100 Block Chesapeake St. SW	28-Oct-23	28-Oct-23	
A1150	Install TAP#2	100 Block Chesapeake St. SW	28-Oct-23	28-Oct-23	
Pavement Restoration			6-Mar-23		
Martin Luther King Jr. Ave. & Ivanhoe Street SW			30-Oct-23		
Utility			30-Oct-23		
Ivanhoe St. SW Utility			4-Feb-24		

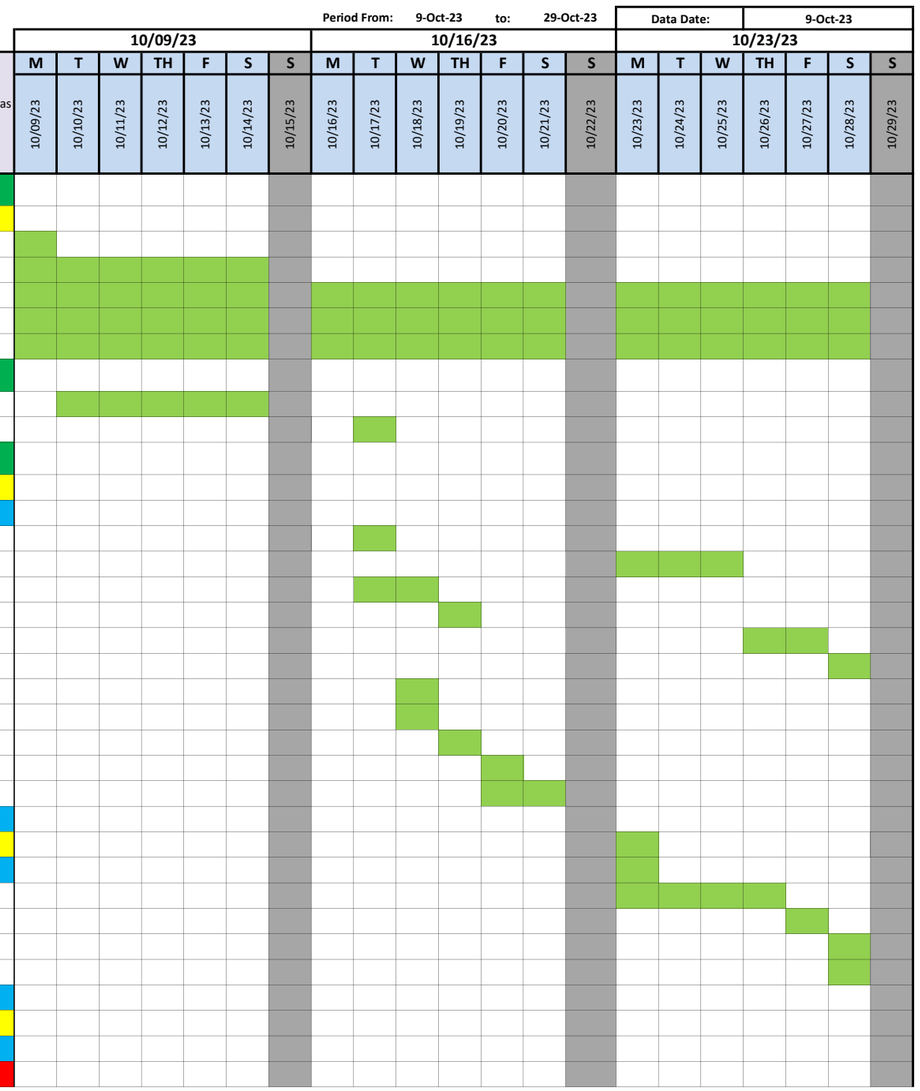

Notes: Saturday works will be requested to DDOT for approval

Procurement of PEPCO Precast Structures: - CPDC plans to collect all precast structures and materials from PEPCO and make them available for use on the project starting October 2, 2023, with Gillespie providing structures on-site or yard delivery.

MA
