DCKA-2022-C-0036-U13DC PLUG Feeder 15009 Civil Construction MOD1-UP13

Classic Schedule Update Layout-F15001_2 DATA DATE: 01-Jul-24

26-Jun-24 15:35

Activity ID	Activity Name	Original Duration	Primary Resource	Start	Finish	Duration % Complete	Total Float
DCKA-2022-C-0036-U13	DC PLUG Feeder 15009 Civil Construction MOD1-UP13	410		01-Mar-23 A	28-Aug-24	89.76%	51
DCKA-2022-C-0036-U13.1	Project Milestones	13		09-Aug-24	28-Aug-24	0%	51
MIL1030	Project Close Out	0			28-Aug-24	0%	76
MIL1035	COI#4 Project Substantial Completion	0			09-Aug-24	0%	64
DCKA-2022-C-0036-U13.2	Construction Milestones	0				0%	0
DCKA-2022-C-0036-U13.3	Submittals and Shop Drawings	0				0%	0
DCKA-2022-C-0036-U13.3.1	General Requirements Submittals	0				0%	0
DCKA-2022-C-0036-U13.3.2	Material Submittal	0				0%	0
DCKA-2022-C-0036-U13.4	Material Fabrication & Precurement	0				0%	0
DCKA-2022-C-0036-U13.5	Project Requirements & Notification	600		01-Mar-23 A	06-Jul-24	99%	129
GEN100	Activity Costs Over Project Duration	600	CPDC-MGMT,CPDC PM/MGM	01-Mar-23 A	06-Jul-24	99%	129
DCKA-2022-C-0036-U13.6	Pre-Construction	0				0%	0
DCKA-2022-C-0036-U13.7	Construction Work	70		05-Jun-24 A	09-Aug-24	58.57%	52
DCKA-2022-C-0036-U13.7.1	Utility Works	0				0%	0
DCKA-2022-C-0036-U13.7.1.1	Phase 1 -Utility	0				0%	0
DCKA-2022-C-0036-U13.7.1.1.1	PH1 STRUCTURE	0				0%	0
DCKA-2022-C-0036-U13.7.1.2	Phase 2 -Utility	0				0%	0
DCKA-2022-C-0036-U13.7.1.2.1	PH2 STRUCTURE	0				0%	0
DCKA-2022-C-0036-U13.7.1.3	Phase 3 -Utility	0				0%	0
DCKA-2022-C-0036-U13.7.1.3.1	PH3 STRUCTURE	0				0%	0
DCKA-2022-C-0036-U13.7.1.4	Phase 4 -Utility	0				0%	0
DCKA-2022-C-0036-U13.7.1.4.1	PHASE 4 STRUCTURE	0				0%	0
DCKA-2022-C-0036-U13.7.2	Civil Works	0				0%	0
DCKA-2022-C-0036-U13.7.2.1	Phase 1	0				0%	0
DCKA-2022-C-0036-U13.7.2.2	Phase 2	0				0%	0
DCKA-2022-C-0036-U13.7.2.3	Phase 3	0				0%	0
DCKA-2022-C-0036-U13.7.2.4	Phase 4	0				0%	0
DCKA-2022-C-0036-U13.7.3	Pavement Marking & Signage	0				0%	0
DCKA-2022-C-0036-U13.7.4	Landscaping	0				0%	0
DCKA-2022-C-0036-U13.7.5	Construction Delays	0		05-Jun-24 A	01-Jul-24	0%	4
DEL-1050	DDOT Initiate & Process COI#4 - Blair Rd and 3rd St TEs	0		05-Jun-24 A	01-Jul-24	0%	4
DCKA-2022-C-0036-U13.7.6	Change Order Work	25		08-Jul-24	09-Aug-24	0%	52
CO-1060	COI#4 - Additional TEs @ Blair Rd and 3rd St	15	CPDC-UTL1,CPDC Utility Crew	08-Jul-24*	26-Jul-24	0%	0
CO-1070	COI#4 - Pavement Restoration	10	CPDC-Civil/PCC,CPDC Civil PC	29-Jul-24	09-Aug-24	0%	52
DCKA-2022-C-0036-U13.8	Substantial Completion	18		05-Aug-24	28-Aug-24	0%	51
FNL1020	Asbuilt Submission	5	CPDC-MGMT,CPDC PM/MGM	05-Aug-24	09-Aug-24	0%	52
FNL1030	Asbuilt Review & Acceptance	10	DDOT/CM Engineer,DDOT/CM E	12-Aug-24	23-Aug-24	0%	52
FNL1050	Project Acceptance & Close Out	5	DDOT/CM Engineer,DDOT/CM E	24-Aug-24	28-Aug-24	0%	76

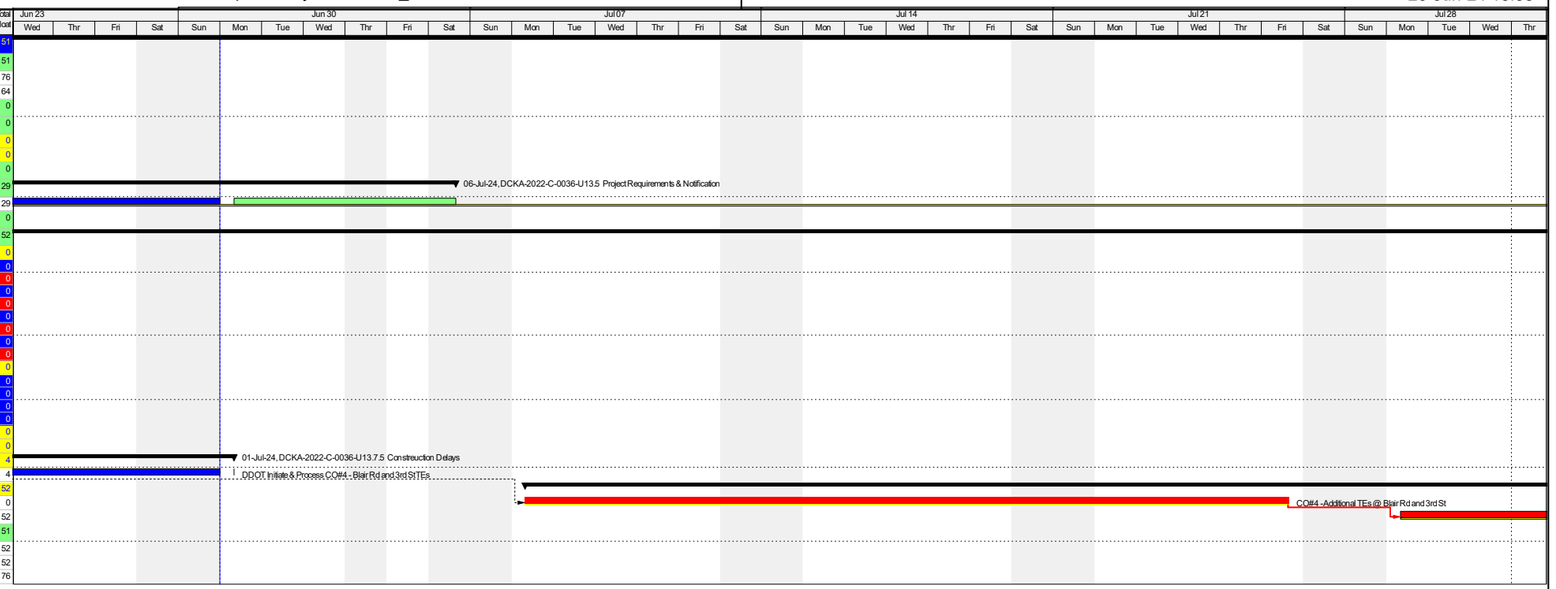

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Baselin...
Milesto...
summary

Page 1 of 1

Date	Revision	Checked	Approved
26-Jun-24	30-Day Look Ahead	JC	

CAPITOL PAVING OF D.C., INC.
WASHINGTON, D.C. 20018
202 - 529-7225
