LOOK AHEAD SCHEDULE

PROJECT: DC PLUG FEEDER 15001 Civil Construction

CAPITOL PAVING OF D.C., INC

Week Start: Mon, 9/16/2024
Today Date: Fri, 9/20/2024
Display Week: 1

ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2023-C-042_BL.3 Submittals and Shop Drawings					**4/3/2024**		**170**
DCKA-2023-C-042_BL.5.1 DUCT INSPECTION							
INS1000	Duct Insp & Cert - PH1	CPDC	Blagden Ter b/w 17th and Colorado Ave	60%	10/1/24	10/4/24	3.00
INS1000	Duct Insp & Cert - PH1	CPDC	Blagden Ave b/w 16th and 18th	0%	10/1/24	10/4/24	3.00
INS1000	Duct Insp & Cert - PH1	CPDC	Colorado Ave NW b/w 16th and 17th St	60%	10/1/24	10/4/24	3.00
DCKA-2023-C-042_BL.6 Pre-Construction					**4/15/2024**		**158**
FAB1010	Order & Procure PEPCO Precast Structures & Conduit 50%	CPDC		80%	5/16/24	10/11/24	149.00
PRE1030	Project Stake Out & Lay Out	CPDC		70%	4/3/24	5/5/25	398.00
PRE1040	Mark Exiting Utilities	CPDC		80%	5/20/24	5/31/24	12.00
	Taking In Situ Soil Sample	CPDC	13th St, Colorado Ave, Madison St, Jefferson St	100%	8/13/24	8/14/24	2.00
DCKA-2023-C-042_BL.7.3 Phase 1.0					**4/29/2024**		**144**
UG Utility					**4/29/2024**		**144**
PH4-UT-1410	Install 6x12 MH9	CPDC-UTL1	1314 Madison st NW	100%	9/16/24	9/20/24	5.00
PH4-UT-1430	Install TMH8	CPDC-UTL1	5617 Colorado Ave NW	100%	9/16/24	9/20/24	5.00
PH4-UT-1480	Install TMH4	CPDC-UTL1	5521 Colorado Ave NW	100%	9/16/24	9/20/24	5.00
PH4-UT-1390	Install 6x12 MH10	CPDC-UTL1	1214 Madison St NW	0%	9/23/24	9/27/24	5.00
PH4-UT-1380	Install SMH3	CPDC-UTL1	1214 Madison St NW	0%	9/23/24	9/27/24	5.00
PH3-UT-1070	Install TMH22	CPDC-UTL1	5104 14th st NW	0%	9/30/24	10/4/24	5.00
PH4-UT-1360	Install 6x12 MH100	CPDC-UTL1	5601 13th St NW	0%	9/30/24	10/4/24	5.00
PH4-UT-1350	Install 6x12 MH99	CPDC-UTL1	5523 13th St NW	0%	9/30/24	10/4/24	5.00
PH4-UT-1250	Install 6x12 MH96a	CPDC-UTL1	5308 13th St NW, Washington, DC	0%	10/7/24	10/11/24	5.00
PH4-UT-1260	Install 6x12 MH97	CPDC-UTL1	5308 13th St NW, Washington, DC	0%	10/7/24	10/11/24	5.00
PH4-UT-1240	Install 6x12 MH96	CPDC-UTL1	5206 13th St NW, Washington, DC	0%	10/14/24	10/18/24	5.00
PH4-UT-1230	Install 6x12 MH95	CPDC-UTL1	5206 13th St NW, Washington, DC	0%	10/14/24	10/18/24	5.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Longefellow St b/w Colorado ave to 13th	0%	8/30/24	8/31/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Ingraham St b/w 14th to Colorado Ave	50%	9/5/24	9/6/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	13th St b/w Madison to Kennedy	100%	9/12/24	9/20/24	9.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	14th St NW b/w Gallatin St & Jefferson	50%	9/24/24	9/25/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	13th St b/w Jeffersn & Ingrham	0%	9/26/24	9/28/24	3.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	13th St b/w Igraham & Hamilton	0%	9/26/24	9/28/24	3.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Jefferson St NW b/w 13th & Georgia	0%	9/27/24	9/30/24	4.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Farragut St b/w 13th & 14th St	0%	10/3/24	10/5/24	3.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Hamilton St b/w 13th & Georgia	0%	10/4/24	10/5/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Jefferson St NW b/w 13th & Georgia	0%	10/4/24	10/5/24	2.00
	Install TEs, THs, 4.5x6 MHs	Miguel E	Jefferson St NW b/w 13th & 14th St	0%	10/10/24	10/12/24	3.00
	Install MH Sump Pit and Grounding PH1	Miguel E		90%	6/17/24	7/5/24	19.00
UG CONDUIT					**4/29/2024**		**144**
PH2-UT-1530	Install Conduit - Decatur b/w 16th St to 18th	CPDC-UTL2		70%	9/6/24	9/27/24	21.00
PH2-UT-1540	Install Conduit - 16th St b/w Decatur to Farragut	CPDC-UTL2		0%	9/30/24	10/11/24	11.00
PH2-UT-1530	Backfill - Decatur b/w 16th to 18th	CPDC-UTL2		70%	9/6/24	9/27/24	21.00
PH2-UT-1540	Backfill - 16th St b/w Decatur to Farragut	CPDC-UTL2		0%	9/30/24	10/11/24	11.00
	MH Recess - Decatur b/w 16th to 18th	CPDC-UTL3		70%	9/6/24	9/27/24	21.00

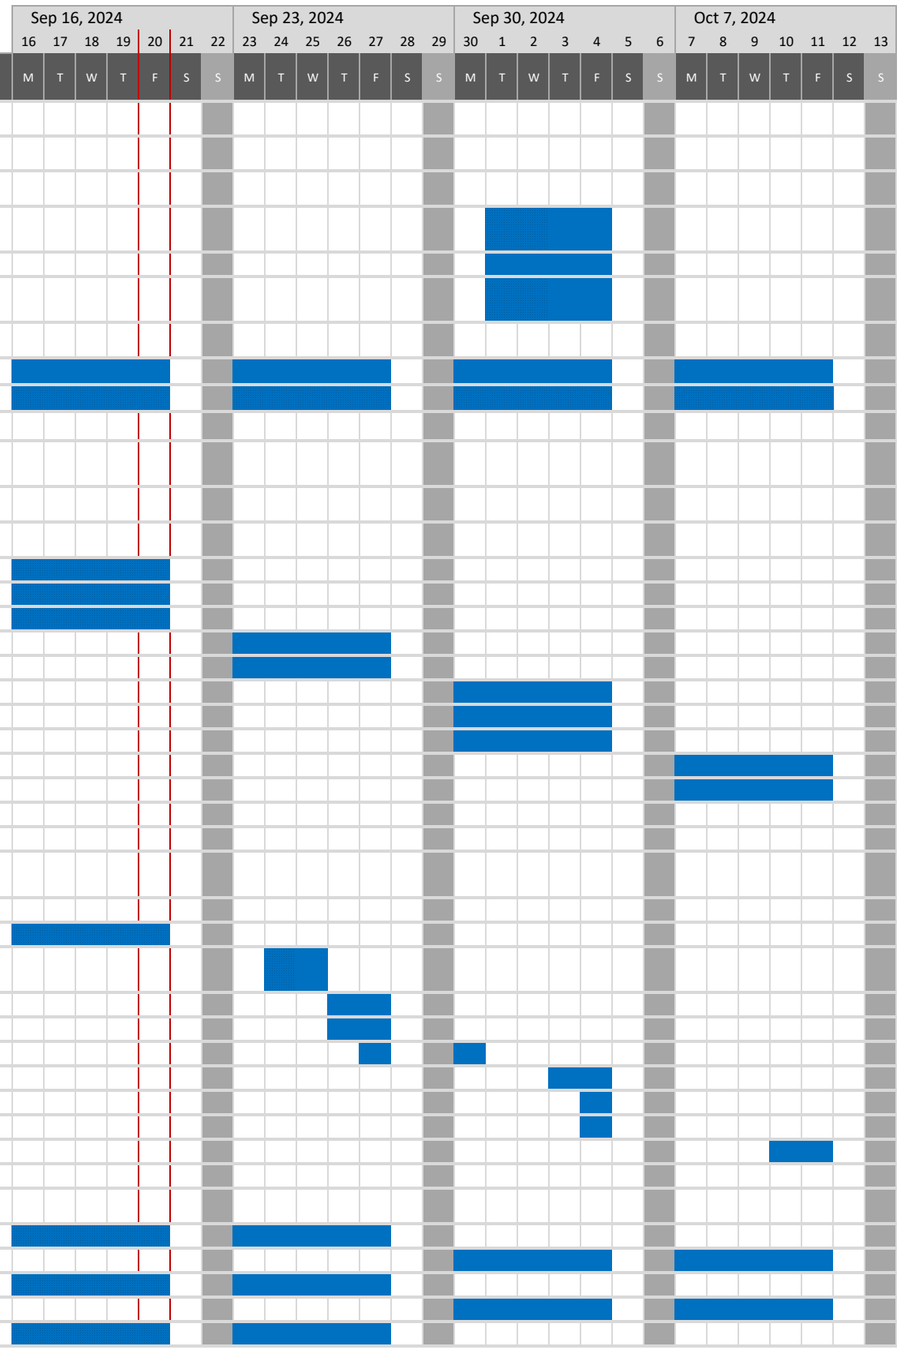

EST. 1987

Display Week: 1

ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
	MH Recess - Decatur b/w 16th to 18th	CPDC-UTL3		0%	9/30/24	10/11/24	11.00
PCC PVMT					**5/24/2024**		**119**
PH1-PVMT-1020	PCC Restoration - Blagden Ave b/w 18th & 17th	CPDC-Armando		100%	8/26/24	8/30/24	4.00
PH1-PVMT-1010	PCC Restoration - Blagden Ave b/w Allison & 18th St	CPDC-Armando		0%	9/24/24	10/4/24	10.00
PH1-PVMT-1000	PCC Restoration - Blagden Ave b/w Allison & Matthew	CPDC-Armando		0%	10/3/24	10/11/24	8.00
ASPHALT PVMT					**6/10/2024**		**102**
PH1-ASPH-1010	Mill & Pave Colorado Ave b/w 16th St and 17th St			100%	8/26/24	8/30/24	4.00
PH1-ASPH-1000	Mill & Pave Blagden Ave b/w 16th St		16th to 18th St	30%	9/4/24	9/6/24	2.00
PVMT MARKINGS					**6/10/2024**		**102**

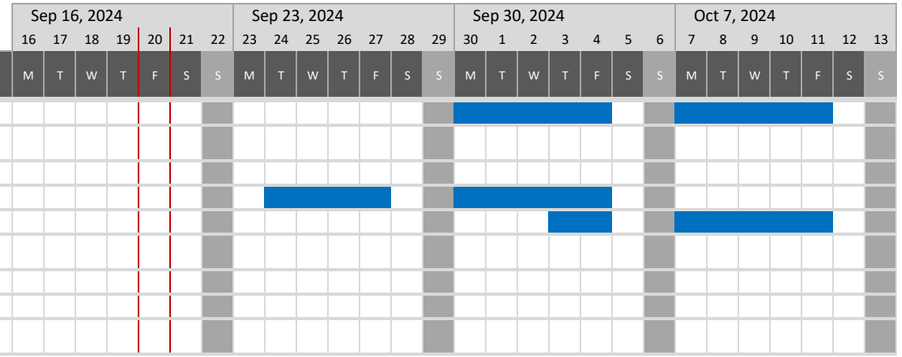

Note: Activities are tentative on weather conditions or other unforseen conditions
Saturday work may be requested on weekly basis to Engineer for review and approval
