TWO WEEK LOOK AHEAD SCHEDULE

PROJECT: DC PLUG FEEDER 15009 Civil Construction

CAPITOL PAVING OF D.C., INC

Week Start: Wed, 3/22/2023
Today Date: Wed, 3/22/2023
Display Week: 1
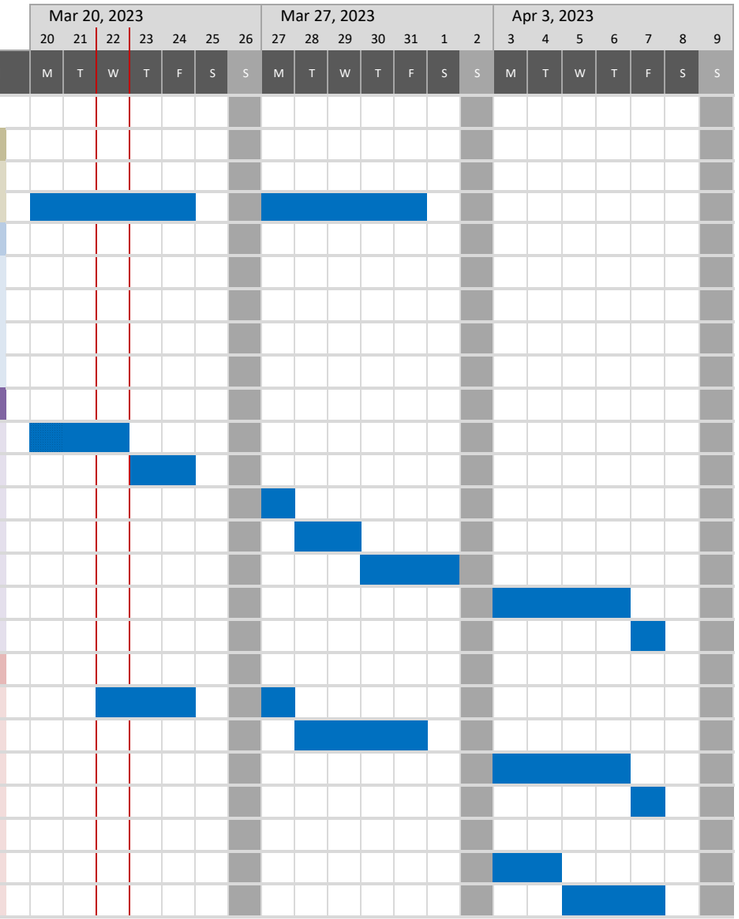
ID	ACTIVITY	RESOURCE	COMMENTS	PROGRESS	START	END	DURATION
DCKA-2022-C-0036.3	**Submittals and Shop Drawings**				**2/15/2023**		**35**
SUB1040	Prepare & Submit - Subsurface DDOT Materials	CPDC		80%	2/15/23	3/17/23	
SUB1060	Engineer's Review & Approval - DDOT Subsurface Materials	CPDC		60%	2/15/23	4/1/23	
DCKA-2022-C-0036.6	**Pre-Construction**				**2/28/2023**		**22**
PRE1030	Project Stake Out & Lay Out	CPDC		30%	2/28/23	3/18/23	18.00
	Collect Soil Samples and Testing PH1	CPDC		25%	3/1/23	3/8/23	7.00
	NTS For Rittenhouse Steet	CPDC		0%	3/8/23	3/9/23	1.00
PRE1050	Project Mobilization	CPDC		50%	2/28/23	3/15/23	15.00
DCKA-2022-C-0036.7.1.2.1	**PH2 STRUCTURE MOD**				**3/13/2023**		**9**
UT2500	Install Structures - Van Buren St b/w 5th & 4th	CPDC1		50%	3/20/23	3/22/23	2.00
UT2510	Install Structures - 4th St b/w Van Buren & Whittier	CPDC1		0%	3/23/23	3/24/23	1.00
UT2520	Install Structures - 4th St b/w Whittier & Aspen	CPDC1		0%	3/25/23	3/27/23	2.00
UT2560	Install Structures - Aspen b/w 5th St & Blair	CPDC1		0%	3/28/23	3/29/23	1.00
UT2530	Install Structures - Whittier St b/w 5th and 3rd	CPDC1		0%	3/30/23	4/1/23	2.00
UT2560	Install Structures - Aspen b/w 5th St & Blair	CPDC1	Large structures	0%	4/3/23	4/6/23	3.00
UT2530	Install Structures - Whittier St b/w 5th and 3rd	CPDC1		0%	4/7/23	4/14/23	7.00
DCKA-2022-C-0036.7.1.2	**Phase 2 - Utility**				**3/21/2022**		**366**
UT2010	Install Conduit - Van Buren St b/w 5th & 4th	CPDC2		0%	3/22/23	3/27/23	5.00
UT2020	Install Conduit - 4th St b/w Van Buren & Whittier	CPDC2		0%	3/28/23	3/31/23	3.00
UT2030	Install Conduit - 4th St b/w Whittier & Aspen	CPDC2		0%	4/3/23	4/6/23	3.00
UT2040	Install Conduit - Aspen b/w 5th St & Blair	CPDC2		0%	4/7/23	4/20/23	13.00
UT2050	Install Conduit - Aspen St b/w 5th & 6th	CPDC2		0%	4/21/23	4/26/23	5.00
UT2120	Install Conduit - 3rd St b/w Whittier & blair	CPDC3		0%	4/3/23	4/4/23	1.00
UT2110	Install Conduit - Whittier St b/w 5th and 3rd	CPDC3		0%	4/5/23	4/14/23	9.00
