Owner: Government of the District of Columbia
Department of Transportation
Project Name: Civil Infrastructure Construction for the District of Columbia Power Line Undergrounding
(DC PLUG) Feeder 15166
Contract No.: DCKA-2023-C-0019

Submitted by:

Capitol Paving of D.C., Inc.
2211 Channing St. NE
Washington, D.C. 20018
202.529.7225

3 WEEK LOOK AHEAD CONSTRUCTION SCHEDULE

Period From: 5-May-25 to: 24-May-25 | Data Date: 28-Apr-25

Activity ID	Description	Location	Resource	Planned Start	Planned Finish	Actual % as of DD
PEPCO Material Fabrication and Procurement				4-Mar-24		100%
Project Requirements				29-May-24		
REQ-1020	Duct Inspection and Certification (Mellon St. SE)	400-500 Blocks Mellon St. SE	CPDC-UTL1	15-Apr-25	16-Apr-25	100%
REQ-1050	Duct Inspection and Certification (Orange St. SE, Oakwood St. SE)	Orange St SE (72' East of 2nd St SE)	CPDC-UTL1	15-Apr-25	16-Apr-25	100%
REQ-1060	Duct Inspection and Certification (Malcolm X Ave. SE)	500 Block Malcolm X Ave. SE	CPDC-UTL1	15-Apr-25	16-Apr-25	100%
Construction Phase				4-Mar-24		
2nd St. SE/Newcomb St. SE				18-Mar-24		
Oakwood St. SE/4th St/5th St/Orange St. SE				4-Apr-24		
Oakwood-1105	~~Install SSB~~#8 Install a 4.5'x6x7' CIP Manhole CHANGE ORDER/MOD 2	Orange St SE (72' East of 2nd St SE	Anchor-UTL1	10-Mar-25	18-Mar-25	100%
Oakwood-1105	Install conduits from TE#38 to CIP Manhole & Pavement Restoration	Orange St SE (72' East of 2nd St SE	CPDC-UTL1	17-Mar-25	25-Apr-25	100%
Malcolm X Ave. SE				13-May-24		
Malcolm-1000	Delete MH#2 (Cast-in-place) _PENDING FOR CHANGE ORDER APPROVAL	Unit Block Malcolm X Ave. SE	Anchor-UTL1	17-Mar-25	20-Mar-25	100%
Malcolm-1000	MH#2 Pavement Restoration	Unit Block Malcolm X Ave. SE	CPDC Civil	23-Apr-25	25-Apr-25	100%
Martin Luther King Jr. Ave. SE				13-May-24		
MLK-1060	MH Penetration and install conduits from Ex. Manhole to TH#6 & Pavement Restoration	2900 Block Martin Luther King Jr. Ave. SE	CPDC Civil	19-Mar-25	25-Apr-25	100%
MLK-1080	PCC Pavement Restoration Martin Luther King Jr. Ave SE- Mellon St. to Malcolm X Ave. PENDING FOR CHANGE ORDER APPROVAL/MODIFICATION (Green Infrastructure Restoration)	2900 Block Martin Luther King Jr. Ave. SE	CPDC Civil	19-May-25	24-May-25	0%
Lebaum St. SE				10-Jun-24		
Mellon St. SE				7-Jun-24		
Mellon-1070	Install 2W conduits to CIP Manhole & Pavement Restoration	465Mellon St. SE	CPDC-Civil	17-Mar-25	25-Apr-25	100%
Mellon-1070	Install conduitsfrom TE#16 to CIP Manhole & Pavement Restoration	511 Mellon St. SE	CPDC-Civil	17-Mar-25	25-Apr-25	100%
Mellon-1070	Install conduits from TH#15 to CIP Manhole & Pavement Restoration	525 Mellon St. SE	CPDC-Civil	17-Mar-25	25-Apr-25	100%
Mellon-1070	Install Topsoil and Seed	Mellon St and 5th St.. SE	CPDC-UTL1	9-Apr-25	14-Apr-25	
Project Closeout				29-May-24		
CLSOUT-1000	Substantial Completion	F15166	CPDC	25-Apr-25	25-Apr-25	100%
CLSOUT-1010	Manhole Inspections	F15166	PEPCO,CM,DDOT	6-May-25	20-May-25	
CLSOUT-1020	Punchlist Items	F15166	CPDC-UTL1	21-May-25	6-Jun-25	

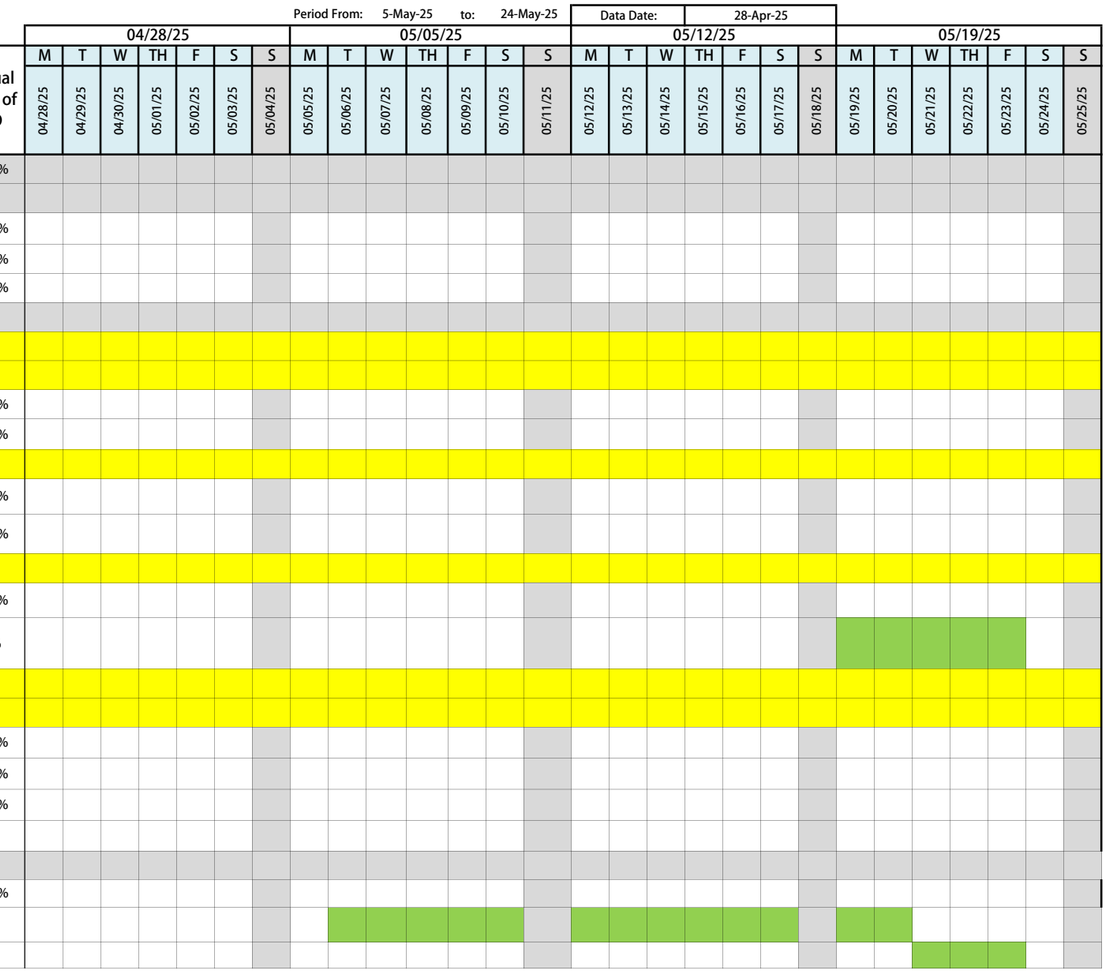

MA
